


Invest in the best regular dividend-paying real estate asset  
**THE COMPACT URBANE CONDOMINIUM FROM RIVERDALE SUITES**

MONTHLY UPDATE  
**FEBRUARY 2021**



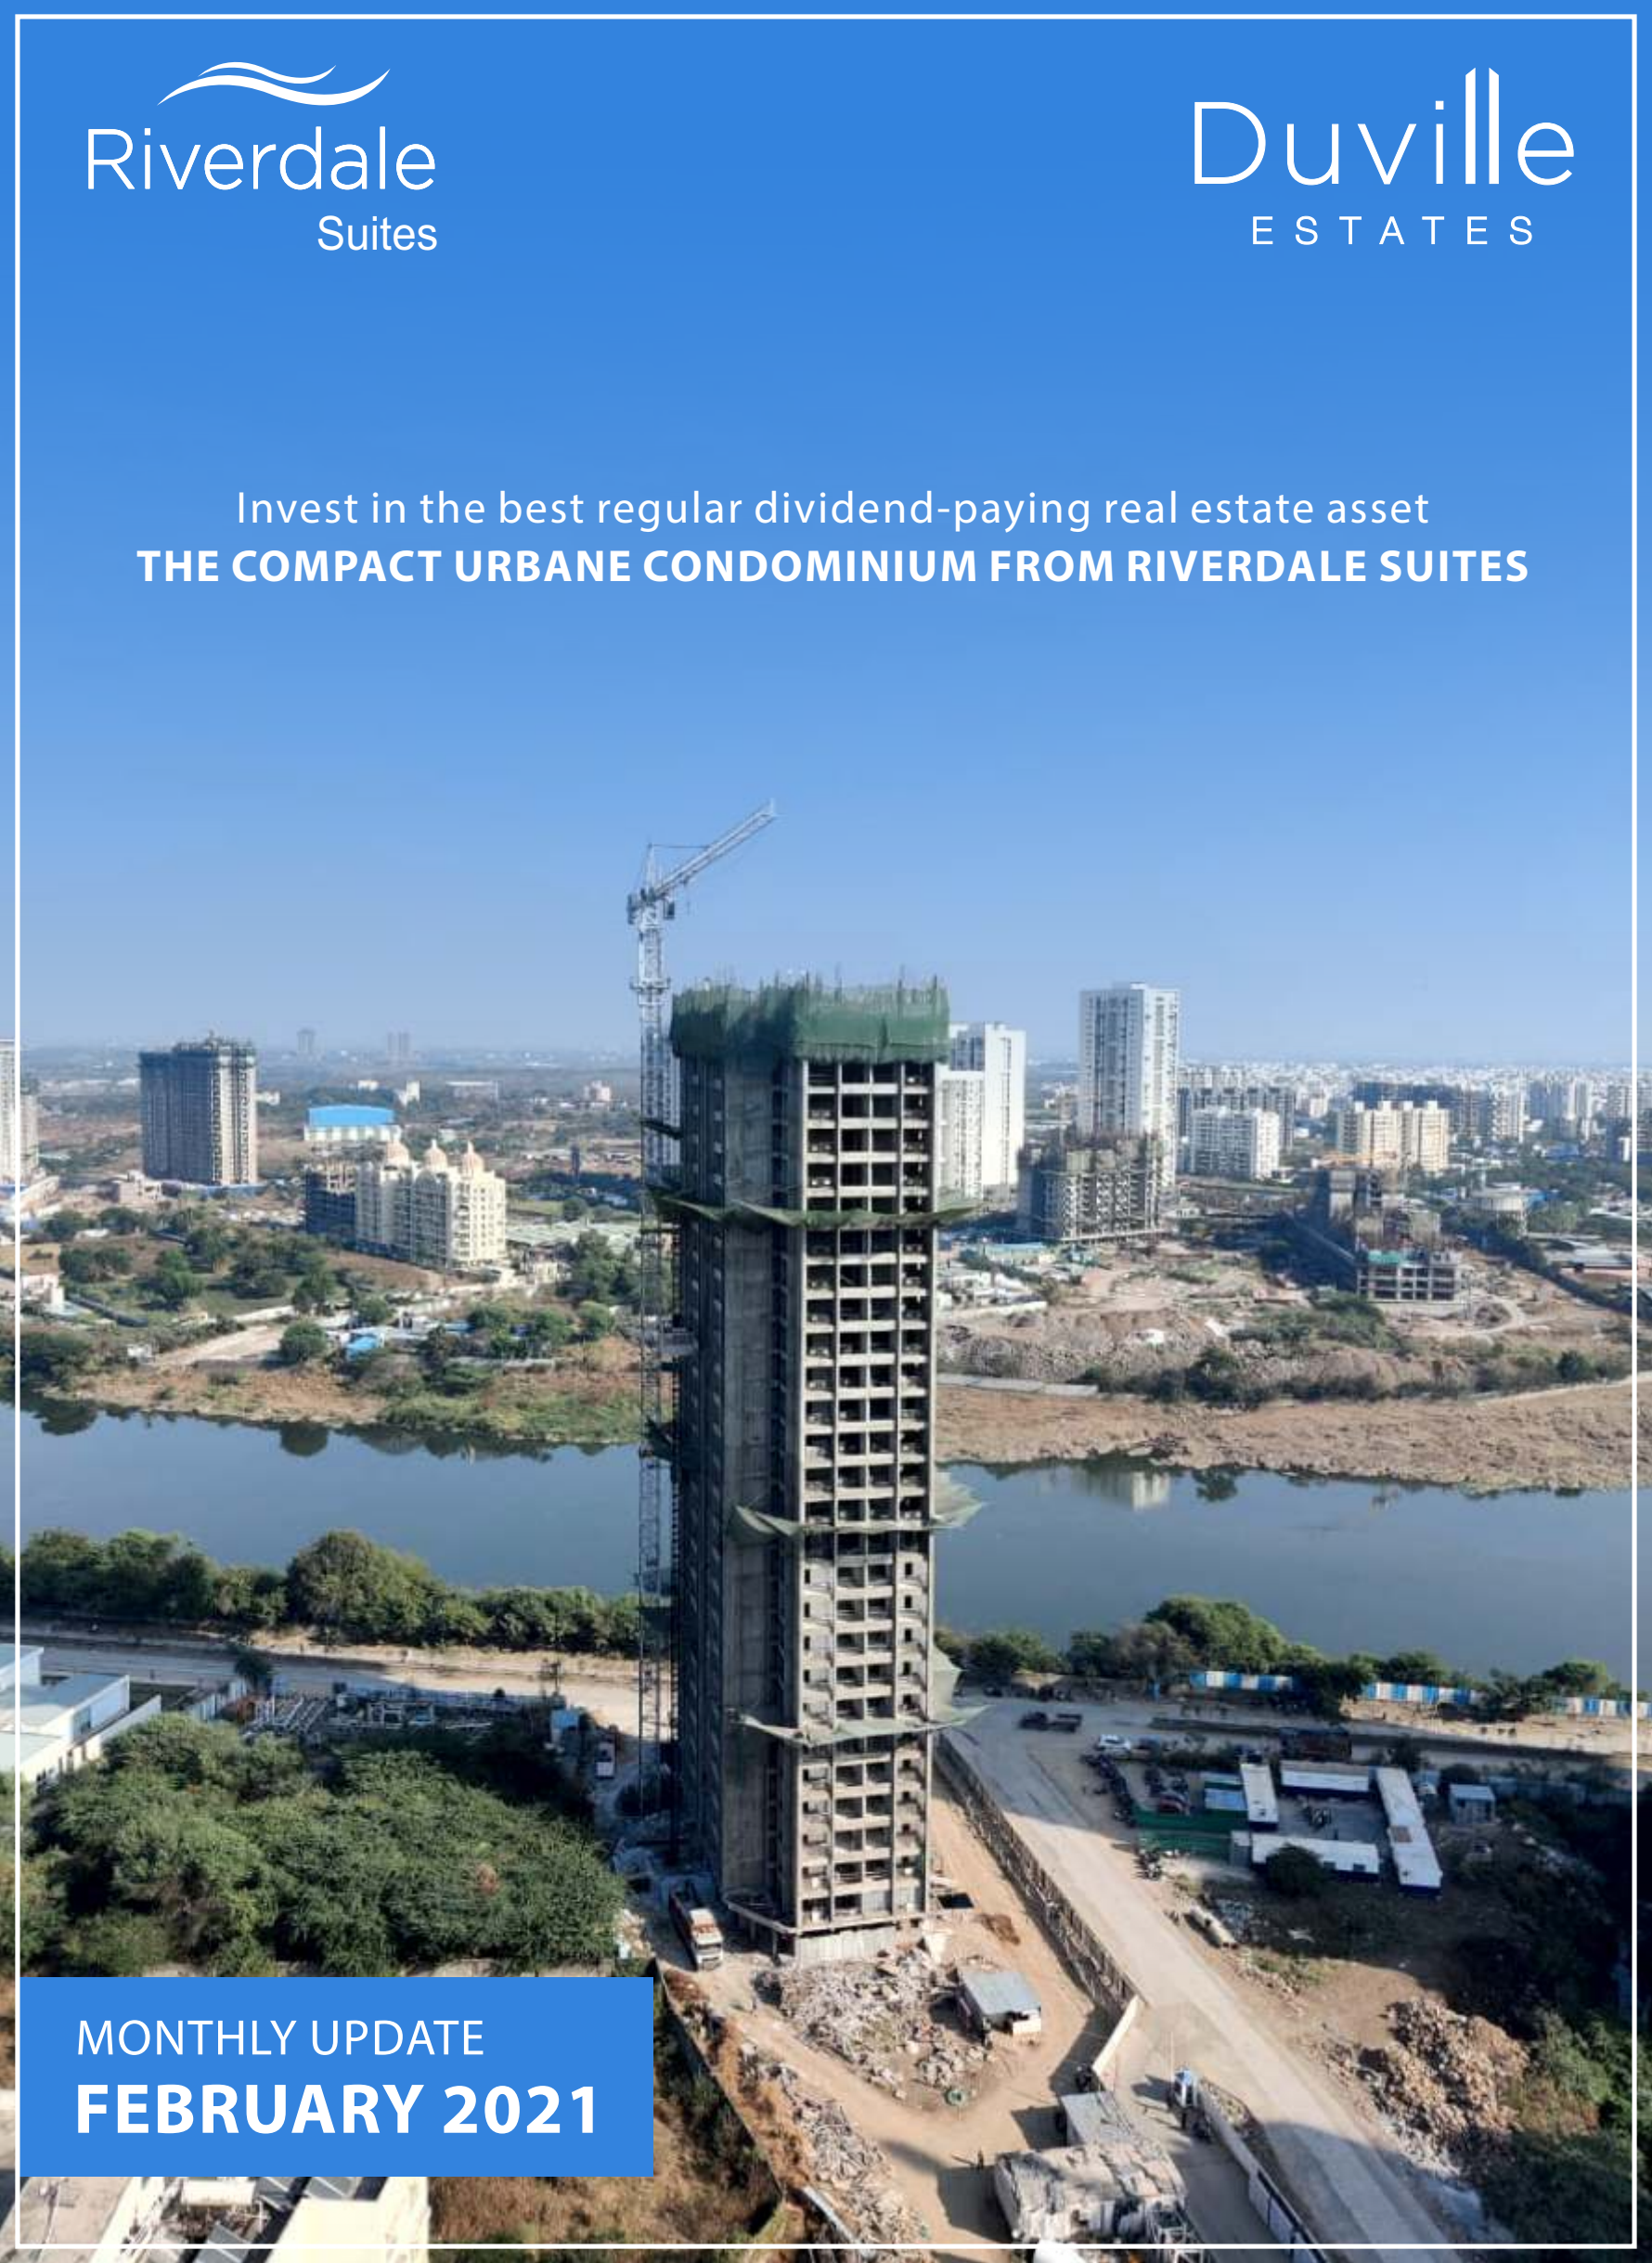

EARN A REFERRAL FEE FROM  
THE COMFORT OF YOUR HOME



Referral Reward Slab

Riverdale  
Residences-I  
₹1,50,000/-

Riverdale  
Heights  
₹1,00,000/-

Riverdale  
Suites  
₹50,000/-

+91 7620 974 974  
www.riverdalepune.com

Construction by  
Shapoorji Pallonji

Development Manager:  
ananta  
LANDWISE PVT LTD

# Riverdale Suites

Riverdale  
Suites



Terrace complete and above Terrace RCC works in progress  
27<sup>th</sup> Aluform assembling & reinforcement work in progress/  
22<sup>nd</sup> Floor AAC Block work-in-progress/ OHWT RCC works in progress



Wall Gypsum 18<sup>th</sup> Floor in progress/ Water-proofing Toilet 1<sup>st</sup> to 10<sup>th</sup> Floor in progress/  
Waterproofing Balcony 4<sup>th</sup> Floor in progress/ 19<sup>th</sup> Floor Electrical conduiting work-in-progress/  
Kitchen Granite Platform 6<sup>th</sup> Floor in progress/ Kitchen Dado fixing 7<sup>th</sup> Floor in progress/  
Tile Flooring 4<sup>th</sup> Floor in progress/ Facade Curtail Glazing survey in progress



Plinth Level PCC, Complete/ Door Frame fixing 11<sup>th</sup> Floor in progress  
Ceiling Gypsum 20<sup>th</sup> Floor in progress/ Lobby Wall Gypsum 16<sup>th</sup> Floor in progress/  
Toilet concealed Plumbing 11<sup>th</sup> Floor in progress/ Plumbing shaft preparation  
started for risers and down-takes



Toilet Drainage 9<sup>th</sup> Floor in progress/ Toilet Dado fixing 6<sup>th</sup> Floor in progress  
Fire Fighting 7<sup>th</sup> Floor in progress/ Staircase inside Block work in progress/  
Plinth level PCC complete/ Sample Flat complete (Series- 3)

